



CANUTILLO INDEPENDENT SCHOOL DISTRICT

CANUTILLO HIGH SCHOOL UPGRADES SCHEDULE

MAJORITY OF CLASSROOMS TO BE COMPLETED ON SUMMER 2026

TIME LINE:

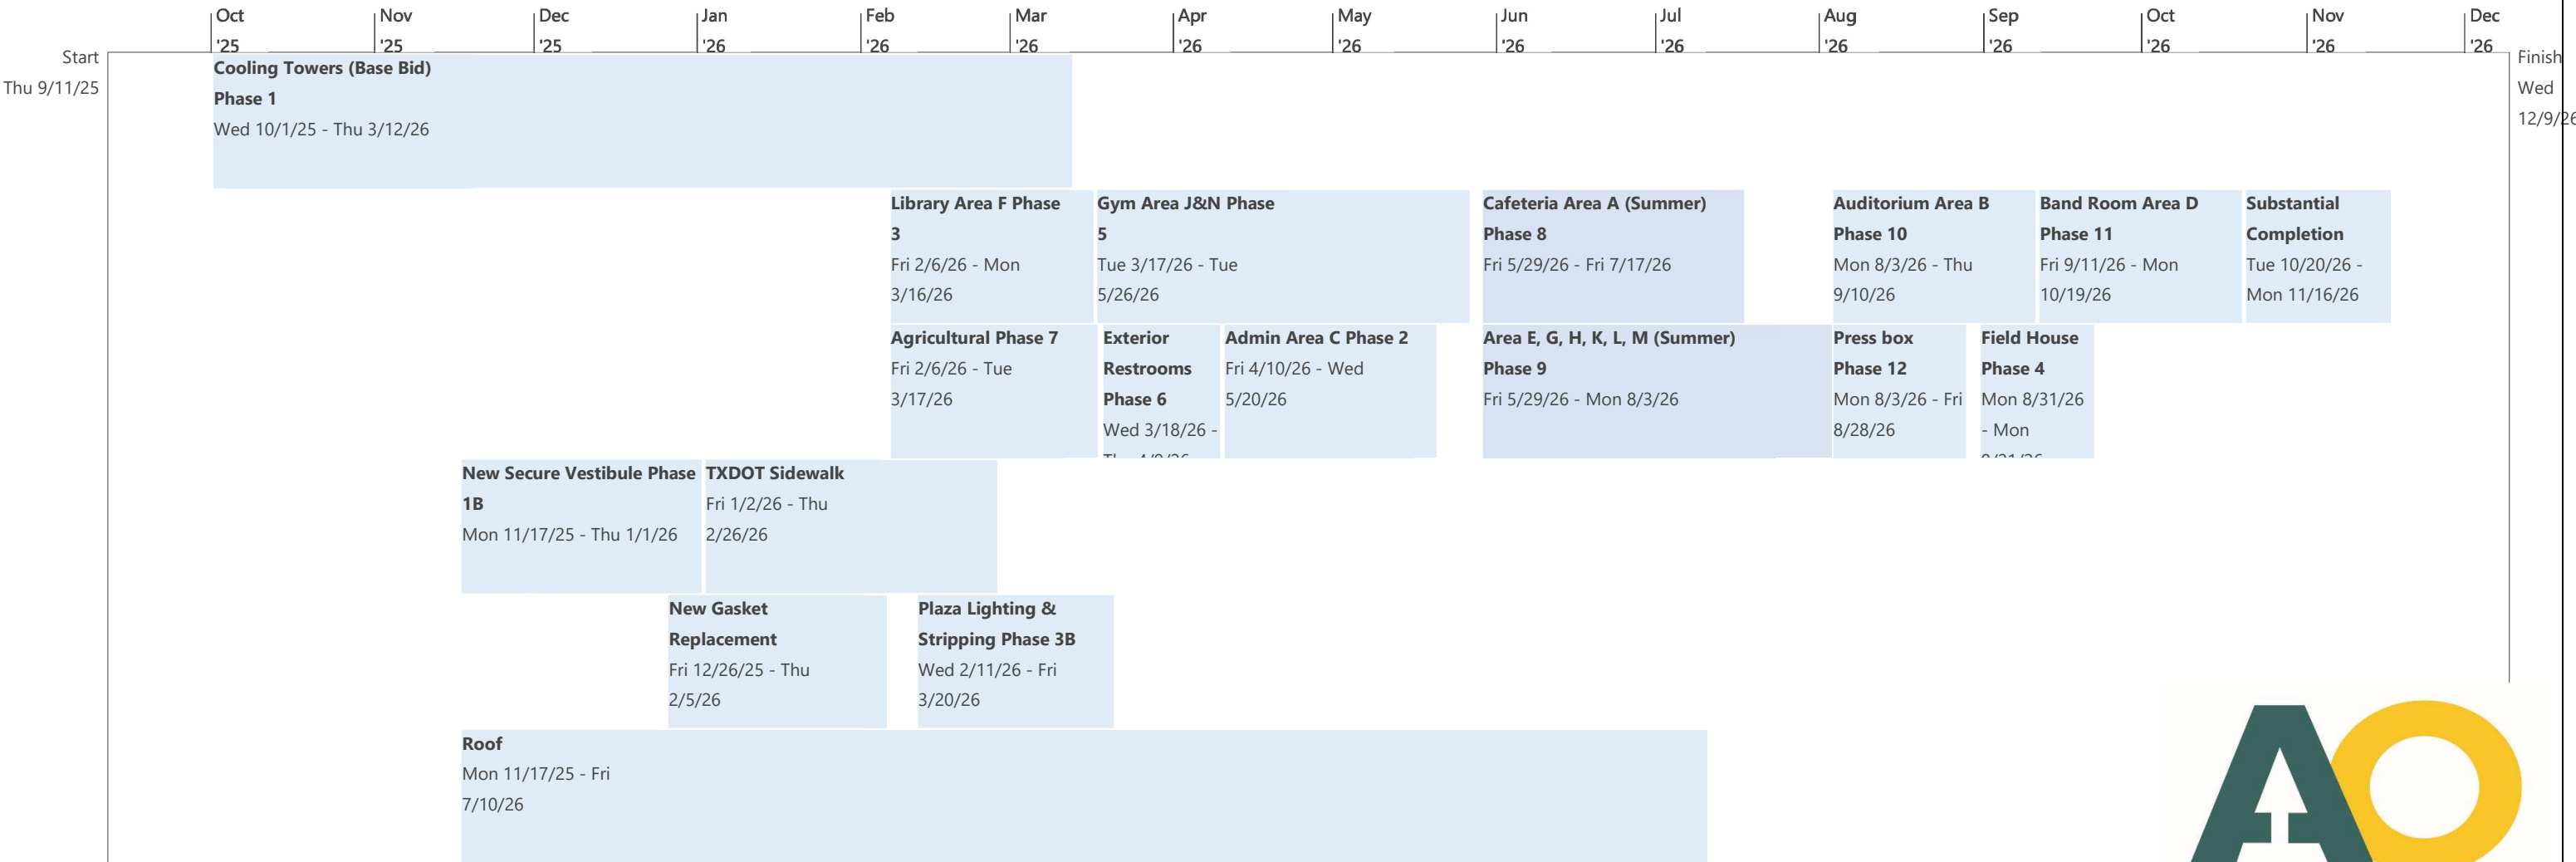

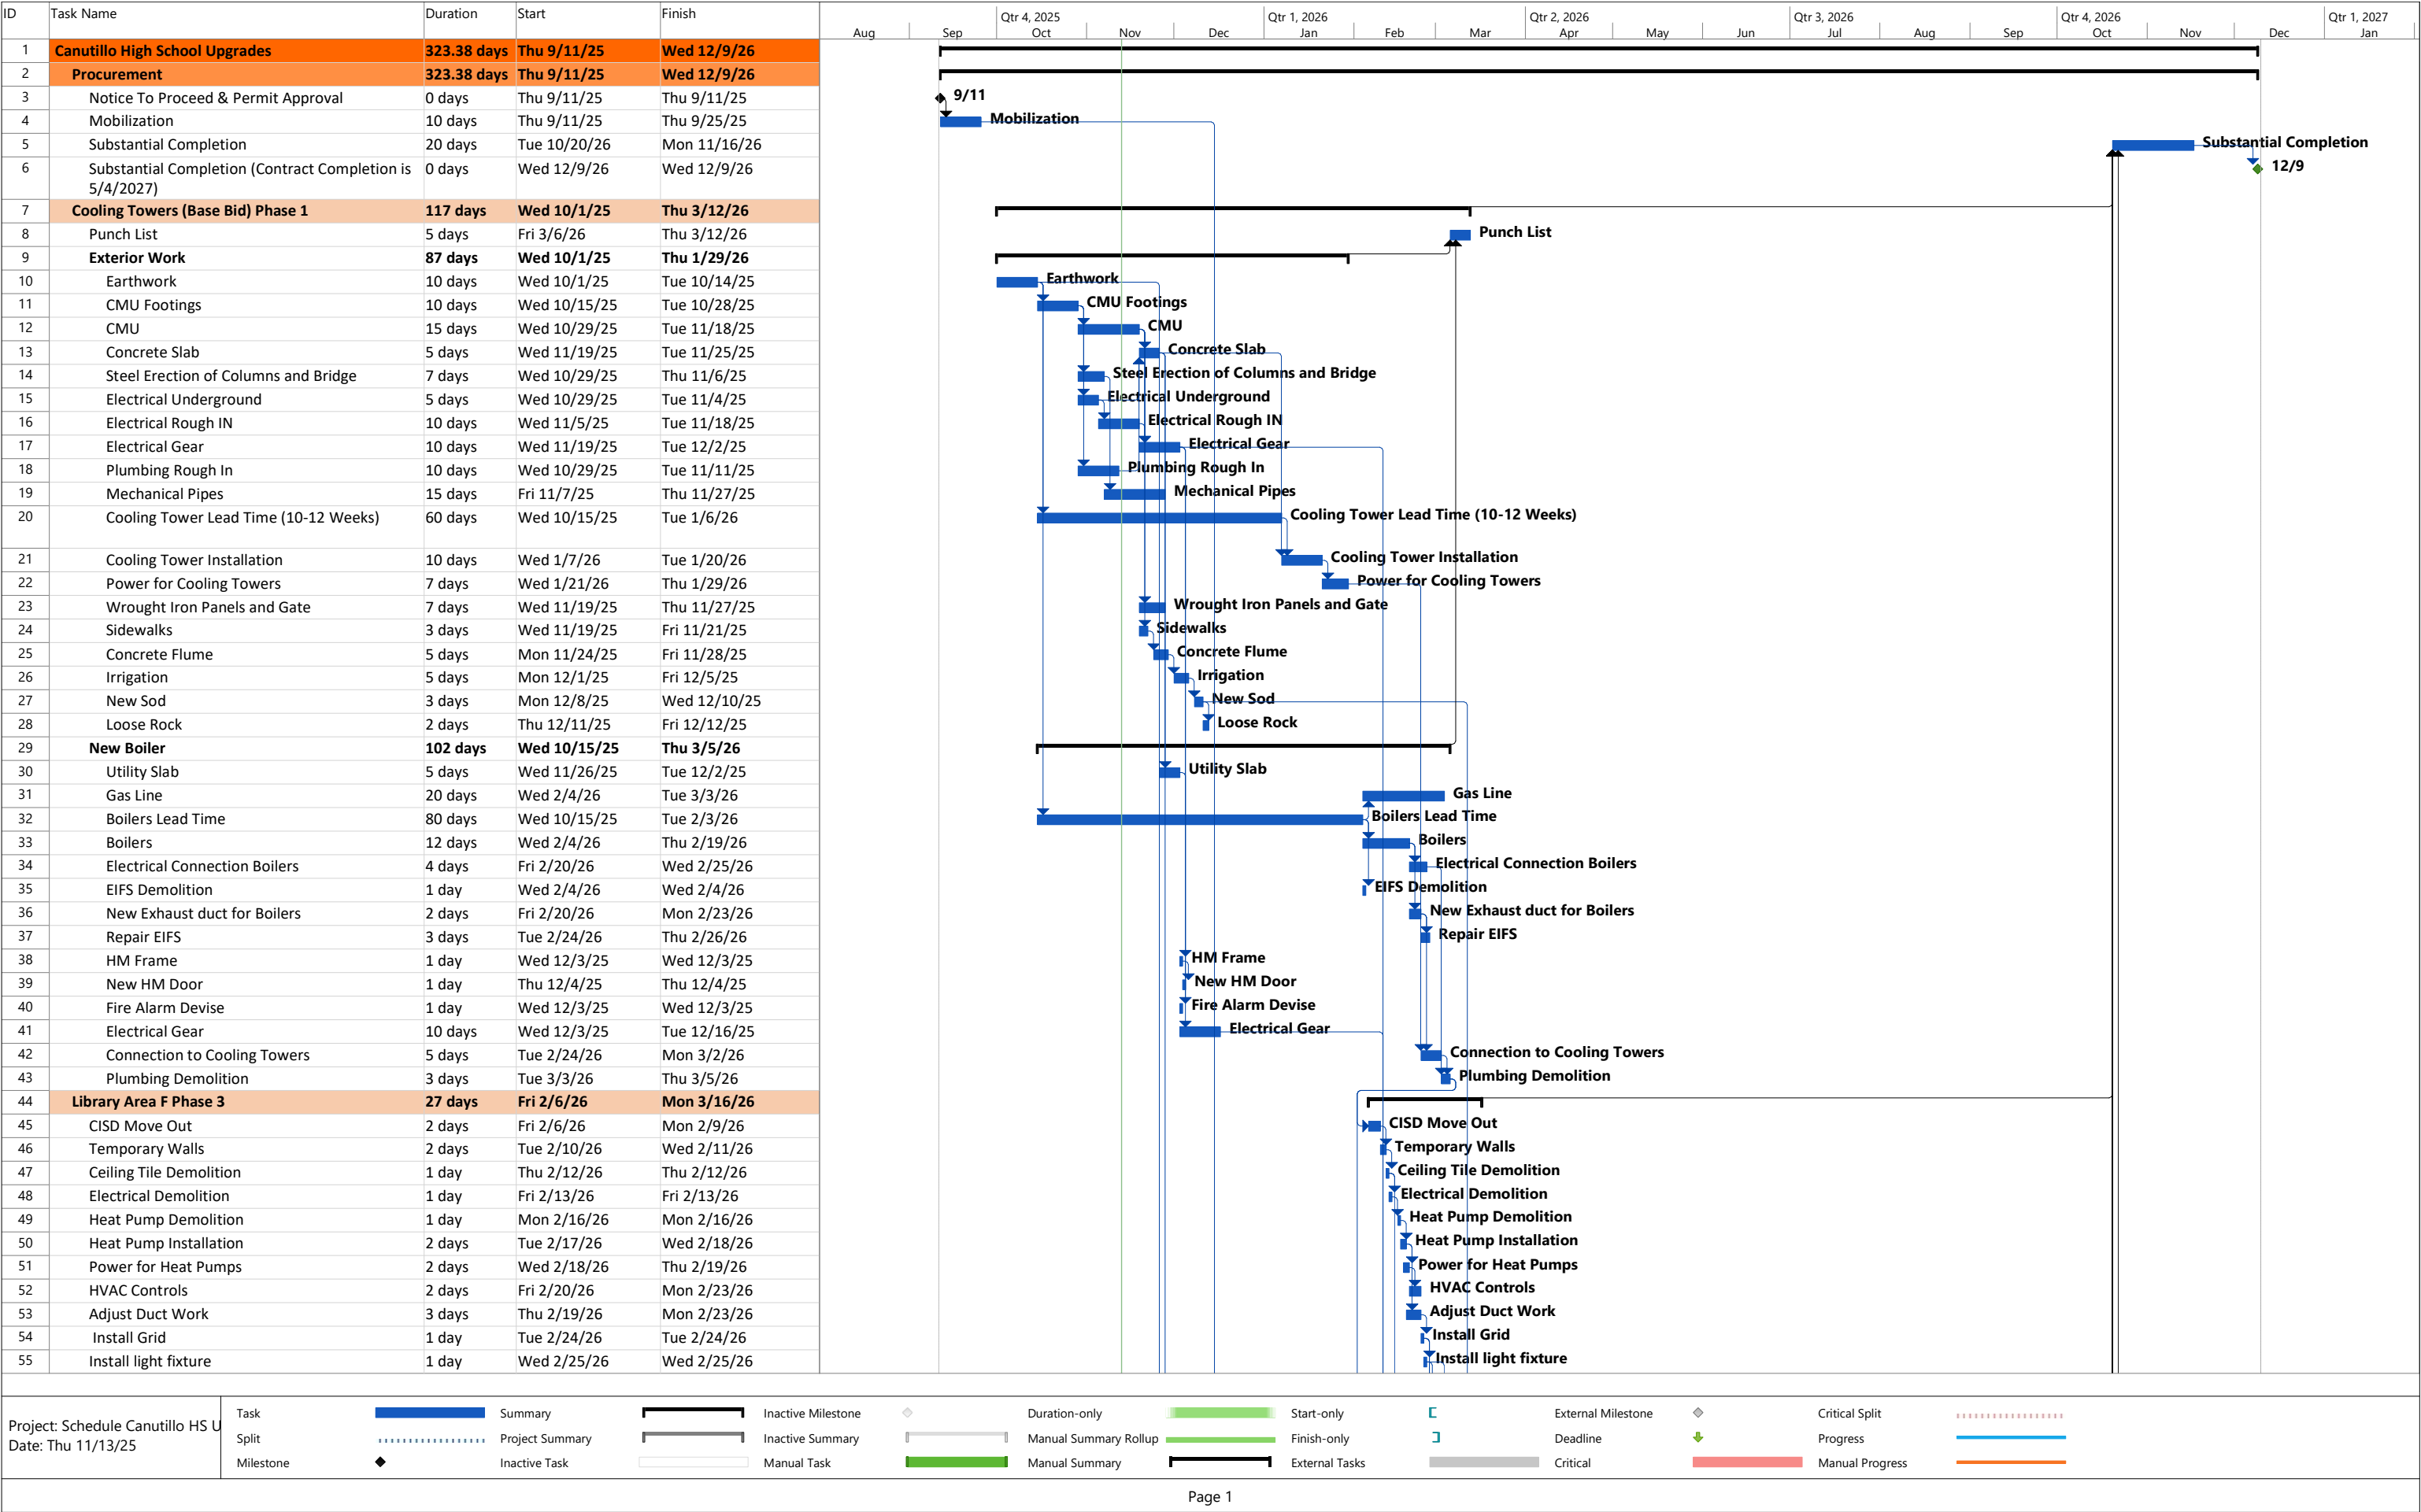

[illegible]

ID	Task Name	Duration	Start	Finish	Aug	Sep	Qtr 4, 2025 Oct	Nov	Dec	Qtr 1, 2026 Jan	Feb	Mar	Qtr 2, 2026 Apr	May	Jun	Qtr 3, 2026 Jul	Aug	Sep	Qtr 4, 2026 Oct	Nov	Dec	Qtr 1, 2027 Jan
113	Heat Pump Installation	13 days	Wed 4/1/26	Fri 4/17/26																		
114	Power for Heat Pumps	8 days	Wed 4/15/26	Fri 4/24/26																		
115	HVAC Controls	3 days	Mon 4/27/26	Wed 4/29/26																		
116	Adjust Duct Work	5 days	Mon 4/20/26	Fri 4/24/26																		
117	Install Grid	2 days	Mon 4/27/26	Tue 4/28/26																		
118	Install light fixture	1 day	Wed 4/29/26	Wed 4/29/26																		
119	Install ceiling tile	1 day	Thu 4/30/26	Thu 4/30/26																		
120	Rough in for Special Systems	15 days	Wed 3/25/26	Tue 4/14/26																		
121	Fire Alarm Devices	10 days	Wed 4/29/26	Tue 5/12/26																		
122	PA Devices	10 days	Wed 4/29/26	Tue 5/12/26																		
123	Final Clean Up	3 days	Wed 5/13/26	Fri 5/15/26																		
124	Final Inspections	18 days	Fri 5/1/26	Tue 5/26/26																		
125	Mechanical Final	1 day	Fri 5/1/26	Fri 5/1/26																		
126	Electrical Final	1 day	Wed 5/13/26	Wed 5/13/26																		
127	Fire Alarm Final	1 day	Wed 5/13/26	Wed 5/13/26																		
128	Fire Final	1 day	Thu 5/14/26	Thu 5/14/26																		
129	Building Final	1 day	Fri 5/15/26	Fri 5/15/26																		
130	Certificate of Completion	1 day	Mon 5/18/26	Mon 5/18/26																		
131	Punch List	5 days	Mon 5/18/26	Fri 5/22/26																		
132	CISD Move In	2 days	Mon 5/25/26	Tue 5/26/26																		
133	Exterior Restrooms Phase 6	17 days	Wed 3/18/26	Thu 4/9/26																		
134	CISD Move Out	1 day	Wed 3/18/26	Wed 3/18/26																		
135	Ceiling Tile Demolition	1 day	Thu 3/19/26	Thu 3/19/26																		
136	Electrical Demolition	1 day	Fri 3/20/26	Fri 3/20/26																		
137	Heat Pump Demolition	1 day	Mon 3/23/26	Mon 3/23/26																		
138	Heat Pump Installation	1 day	Tue 3/24/26	Tue 3/24/26																		
139	Power for Heat Pumps	1 day	Wed 3/25/26	Wed 3/25/26																		
140	HVAC Controls	1 day	Thu 3/26/26	Thu 3/26/26																		
141	Adjust Duct Work	1 day	Wed 3/25/26	Wed 3/25/26																		
142	Install Grid	1 day	Thu 3/26/26	Thu 3/26/26																		
143	Install light fixture	1 day	Fri 3/27/26	Fri 3/27/26																		
144	Install ceiling tile	1 day	Mon 3/30/26	Mon 3/30/26																		
145	Rough in for Special Systems	3 days	Fri 3/20/26	Tue 3/24/26																		
146	Fire Alarm Devices	2 days	Fri 3/27/26	Mon 3/30/26																		
147	PA Devices	2 days	Fri 3/27/26	Mon 3/30/26																		
148	Final Clean Up	1 day	Tue 3/31/26	Tue 3/31/26																		
149	Final Inspections	8 days	Tue 3/31/26	Thu 4/9/26																		
150	Mechanical Final	1 day	Tue 3/31/26	Tue 3/31/26																		
151	Electrical Final	1 day	Tue 3/31/26	Tue 3/31/26																		
152	Fire Alarm Final	1 day	Tue 3/31/26	Tue 3/31/26																		
153	Fire Final	1 day	Wed 4/1/26	Wed 4/1/26																		
154	Building Final	1 day	Thu 4/2/26	Thu 4/2/26																		
155	Certificate of Completion	1 day	Fri 4/3/26	Fri 4/3/26																		
156	Punch List	5 days	Wed 4/1/26	Tue 4/7/26																		
157	CISD Move In	2 days	Wed 4/8/26	Thu 4/9/26																		
158	Admin Area C Phase 2	29 days	Fri 4/10/26	Wed 5/20/26																		
159	CISD Move Out	2 days	Fri 4/10/26	Mon 4/13/26																		
160	Temporary Walls	2 days	Tue 4/14/26	Wed 4/15/26																		
161	Ceiling Tile Demolition	1 day	Thu 4/16/26	Thu 4/16/26																		
162	Electrical Demolition	1 day	Thu 4/16/26	Thu 4/16/26																		
163	Heat Pump Demolition	1 day	Fri 4/17/26	Fri 4/17/26																		
164	Heat Pump Installation	3 days	Mon 4/20/26	Wed 4/22/26																		
165	Power for Heat Pumps	3 days	Wed 4/22/26	Fri 4/24/26																		
166	HVAC Controls	3 days	Mon 4/27/26	Wed 4/29/26																		
167	Adjust Duct Work	3 days	Thu 4/23/26	Mon 4/27/26																		
168	Install Grid	2 days	Tue 4/28/26	Wed 4/29/26																		
169	Install light fixture	1 day	Thu 4/30/26	Thu 4/30/26																		

Project: Schedule Canutillo HS U

Date: Thu 11/13/25

Task

Split

Milestone

.....

◆

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

◇

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

◇

↓


Critical Split

Progress

Manual Progress

.....

Page 3

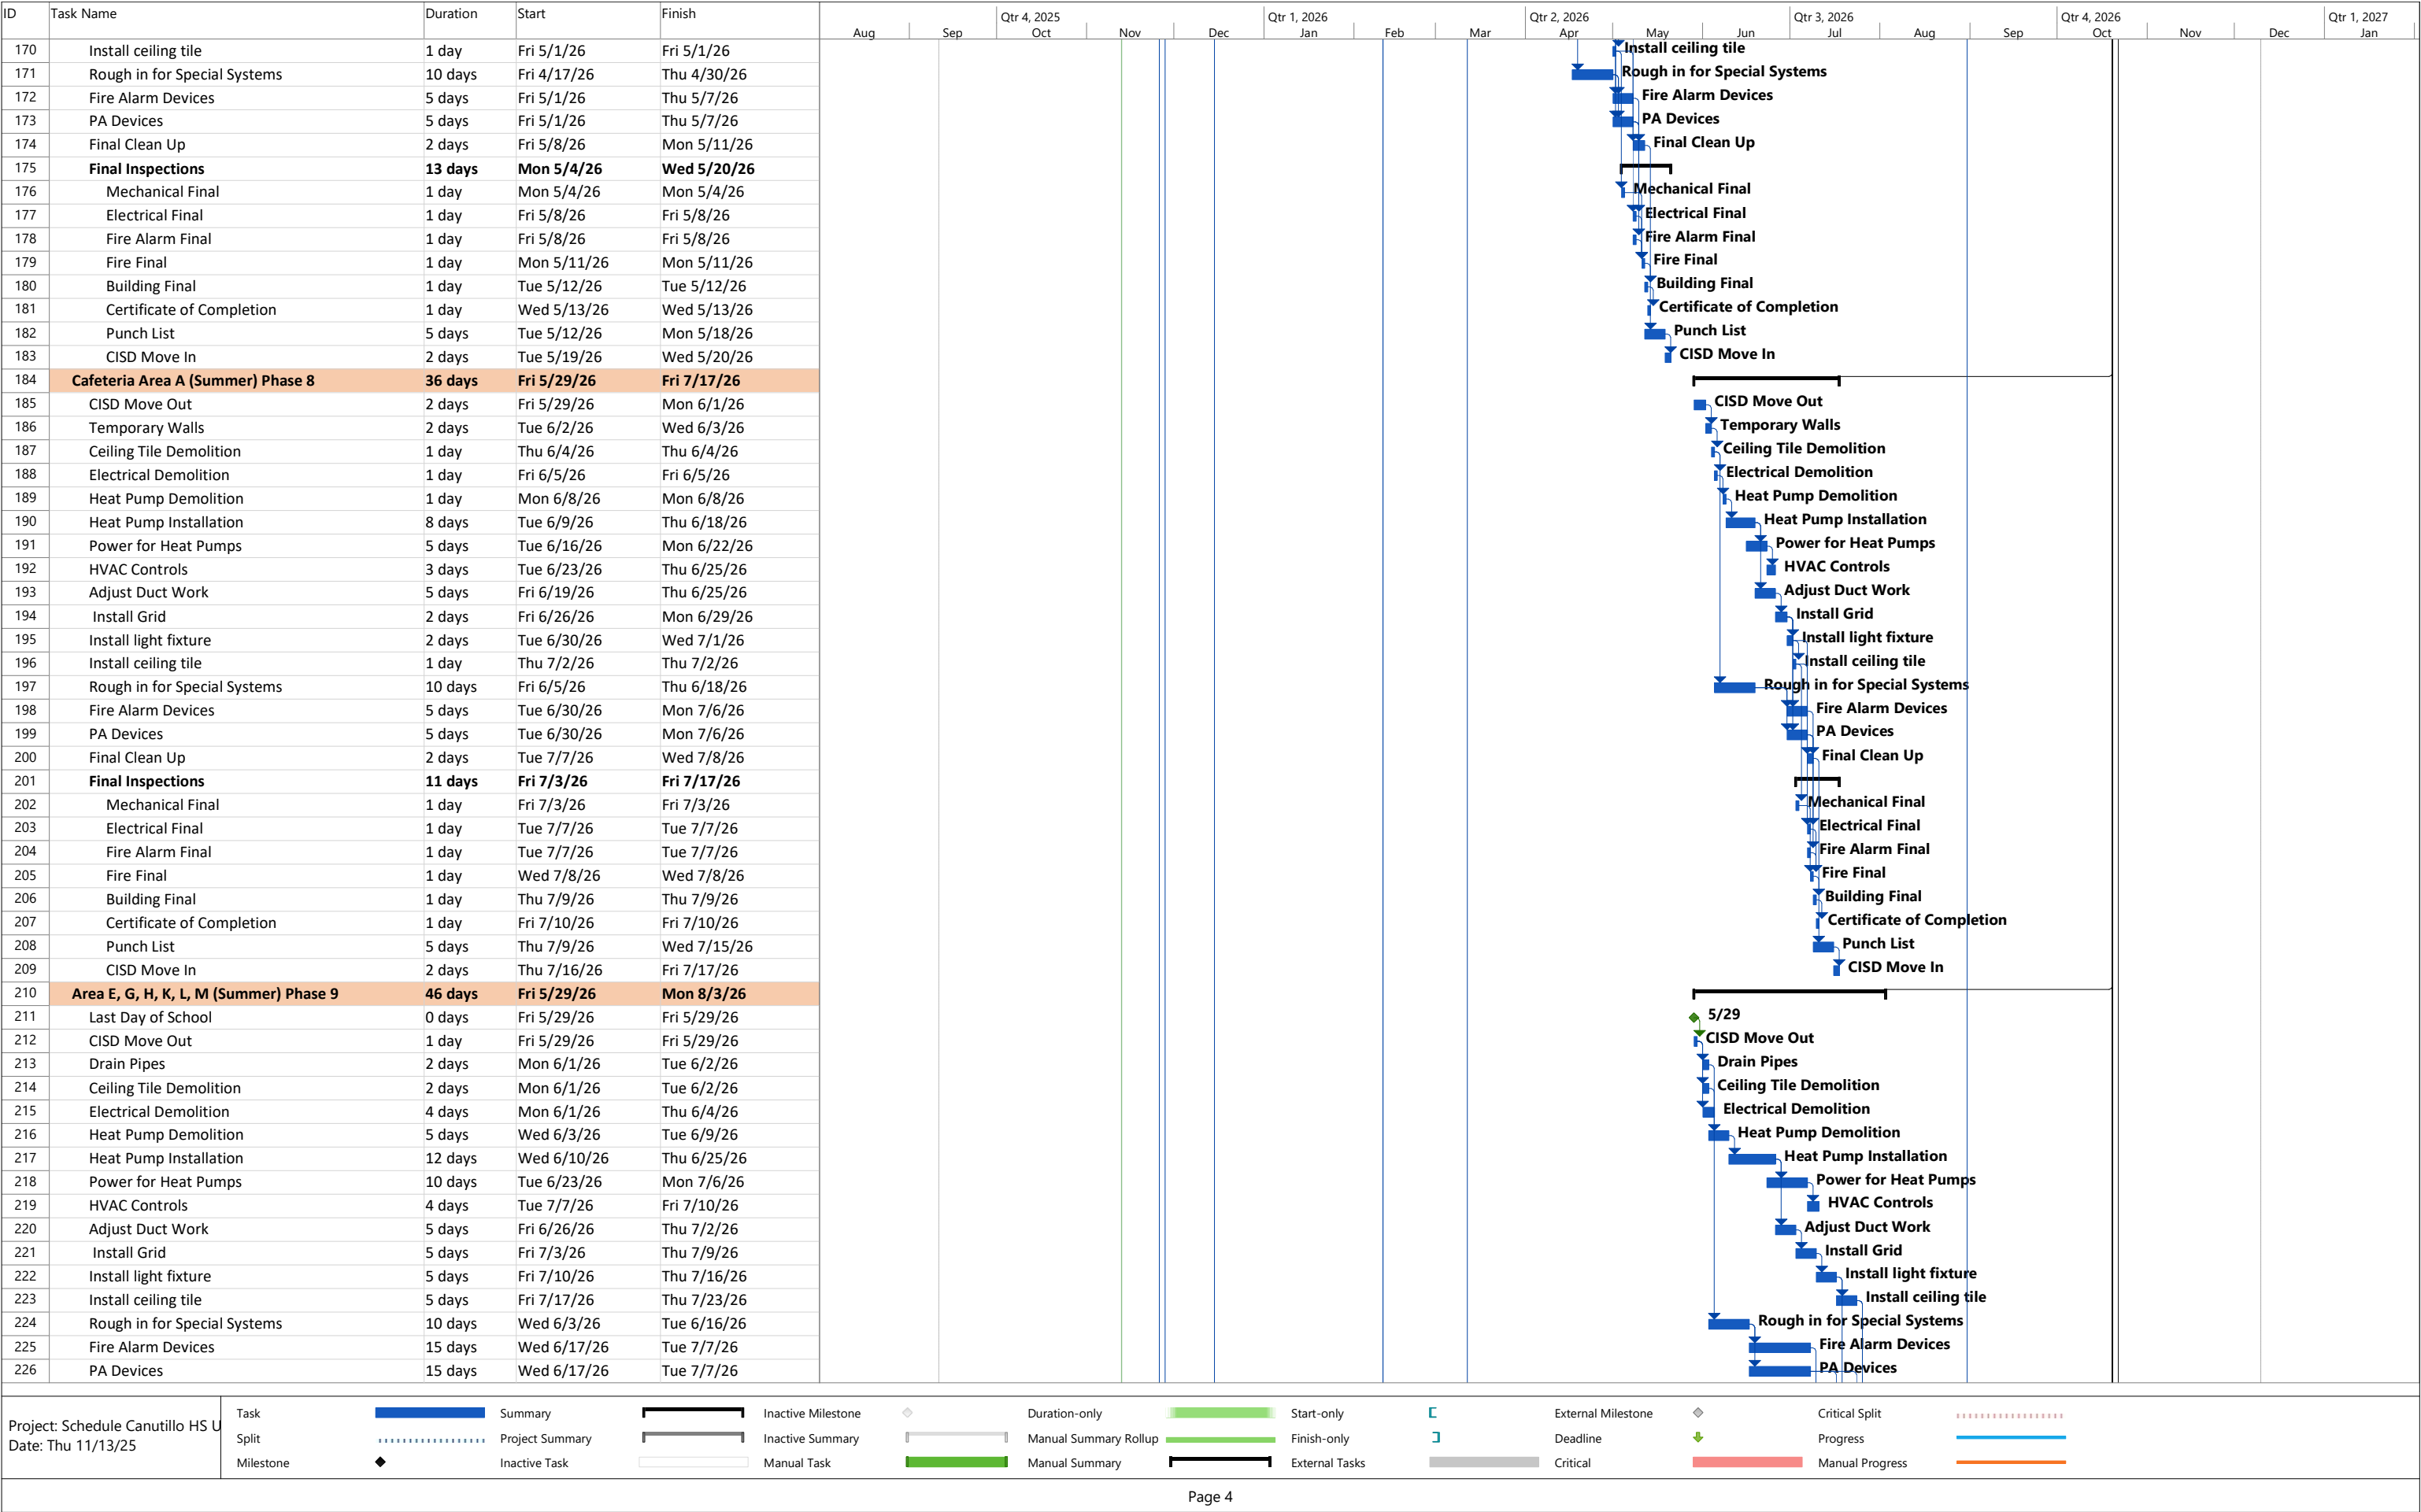

ID	Task Name	Duration	Start	Finish	Aug	Sep	Qtr 4, 2025 Oct	Nov	Dec	Qtr 1, 2026 Jan	Feb	Mar	Qtr 2, 2026 Apr	May	Jun	Qtr 3, 2026 Jul	Aug	Sep	Qtr 4, 2026 Oct	Nov	Dec	Qtr 1, 2027 Jan
227	Final Clean Up	5 days	Fri 7/24/26	Thu 7/30/26																		
228	Final Inspections	18 days	Wed 7/8/26	Mon 8/3/26																		
229	Mechanical Final	1 day	Fri 7/24/26	Fri 7/24/26																		
230	Electrical Final	1 day	Fri 7/17/26	Fri 7/17/26																		
231	Fire Alarm Final	1 day	Wed 7/8/26	Wed 7/8/26																		
232	Fire Final	1 day	Mon 7/27/26	Mon 7/27/26																		
233	Building Final	1 day	Tue 7/28/26	Tue 7/28/26																		
234	Certificate of Completion	1 day	Wed 7/29/26	Wed 7/29/26																		
235	CISD Move In	2 days	Thu 7/30/26	Fri 7/31/26																		
236	Teacher's Move In	0 days	Mon 7/27/26	Mon 7/27/26																		
237	First Day of School 2026-2027	0 days	Mon 8/3/26	Mon 8/3/26																		
238	Auditorium Area B Phase 10	29 days	Mon 8/3/26	Thu 9/10/26																		
239	CISD Move Out	2 days	Mon 8/3/26	Tue 8/4/26																		
240	Temporary Walls	2 days	Wed 8/5/26	Thu 8/6/26																		
241	Ceiling Tile Demolition	1 day	Fri 8/7/26	Fri 8/7/26																		
242	Electrical Demolition	2 days	Fri 8/7/26	Mon 8/10/26																		
243	Heat Pump Demolition	1 day	Tue 8/11/26	Tue 8/11/26																		
244	Heat Pump Installation	4 days	Wed 8/12/26	Mon 8/17/26																		
245	Power for Heat Pumps	4 days	Thu 8/13/26	Tue 8/18/26																		
246	HVAC Controls	3 days	Wed 8/19/26	Fri 8/21/26																		
247	Adjust Duct Work	3 days	Tue 8/18/26	Thu 8/20/26																		
248	Install Grid	1 day	Fri 8/21/26	Fri 8/21/26																		
249	Install light fixture	1 day	Mon 8/24/26	Mon 8/24/26																		
250	Install ceiling tile	1 day	Tue 8/25/26	Tue 8/25/26																		
251	Rough in for Special Systems	10 days	Mon 8/10/26	Fri 8/21/26																		
252	Fire Alarm Devices	5 days	Mon 8/24/26	Fri 8/28/26																		
253	PA Devices	5 days	Mon 8/24/26	Fri 8/28/26																		
254	Final Clean Up	2 days	Mon 8/31/26	Tue 9/1/26																		
255	Final Inspections	12 days	Wed 8/26/26	Thu 9/10/26																		
256	Mechanical Final	1 day	Wed 8/26/26	Wed 8/26/26																		
257	Electrical Final	1 day	Mon 8/31/26	Mon 8/31/26																		
258	Fire Alarm Final	1 day	Mon 8/31/26	Mon 8/31/26																		
259	Fire Final	1 day	Tue 9/1/26	Tue 9/1/26																		
260	Building Final	1 day	Wed 9/2/26	Wed 9/2/26																		
261	Certificate of Completion	1 day	Thu 9/3/26	Thu 9/3/26																		
262	Punch List	5 days	Wed 9/2/26	Tue 9/8/26																		
263	CISD Move In	2 days	Wed 9/9/26	Thu 9/10/26																		
264	Band Room Area D Phase 11	27 days	Fri 9/11/26	Mon 10/19/26																		
265	CISD Move Out	2 days	Fri 9/11/26	Mon 9/14/26																		
266	Temporary Walls	2 days	Tue 9/15/26	Wed 9/16/26																		
267	Ceiling Tile Demolition	1 day	Thu 9/17/26	Thu 9/17/26																		
268	Electrical Demolition	1 day	Fri 9/18/26	Fri 9/18/26																		
269	Heat Pump Demolition	1 day	Fri 9/18/26	Fri 9/18/26																		
270	Heat Pump Installation	3 days	Fri 9/18/26	Tue 9/22/26																		
271	Power for Heat Pumps	3 days	Mon 9/21/26	Wed 9/23/26																		
272	HVAC Controls	3 days	Thu 9/24/26	Mon 9/28/26																		
273	Adjust Duct Work	3 days	Wed 9/23/26	Fri 9/25/26																		
274	Install Grid	2 days	Mon 9/28/26	Tue 9/29/26																		
275	Install light fixture	1 day	Wed 9/30/26	Wed 9/30/26																		
276	Install ceiling tile	1 day	Thu 10/1/26	Thu 10/1/26																		
277	Rough in for Special Systems	7 days	Fri 9/18/26	Mon 9/28/26																		
278	Fire Alarm Devices	5 days	Wed 9/30/26	Tue 10/6/26																		
279	PA Devices	5 days	Wed 9/30/26	Tue 10/6/26																		
280	Final Clean Up	2 days	Wed 10/7/26	Thu 10/8/26																		
281	Final Inspections	12 days	Fri 10/2/26	Mon 10/19/26																		
282	Mechanical Final	1 day	Fri 10/2/26	Fri 10/2/26																		
283	Electrical Final	1 day	Wed 10/7/26	Wed 10/7/26																		

Project: Schedule Canutillo HS U

Date: Thu 11/13/25

Task

Split

Milestone

.....

◆

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

◆

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

◆

↓

Critical Split

Progress

Manual Progress

.....

Page 5

ID	Task Name	Duration	Start	Finish	Aug	Sep	Qtr 4, 2025 Oct	Nov	Dec	Qtr 1, 2026 Jan	Feb	Mar	Qtr 2, 2026 Apr	May	Jun	Qtr 3, 2026 Jul	Aug	Sep	Qtr 4, 2026 Oct	Nov	Dec	Qtr 1, 2027 Jan
284	Fire Alarm Final	1 day	Wed 10/7/26	Wed 10/7/26																		
285	Fire Final	1 day	Thu 10/8/26	Thu 10/8/26																		
286	Building Final	1 day	Fri 10/9/26	Fri 10/9/26																		
287	Certificate of Completion	1 day	Mon 10/12/26	Mon 10/12/26																		
288	Punch List	5 days	Fri 10/9/26	Thu 10/15/26																		
289	CISD Move In	2 days	Fri 10/16/26	Mon 10/19/26																		
290	Press box Phase 12	20 days	Mon 8/3/26	Fri 8/28/26																		
291	CISD Move Out	1 day	Mon 8/3/26	Mon 8/3/26																		
292	Ceiling Tile Demolition	1 day	Tue 8/4/26	Tue 8/4/26																		
293	Electrical Demolition	1 day	Wed 8/5/26	Wed 8/5/26																		
294	Heat Pump Demolition	1 day	Thu 8/6/26	Thu 8/6/26																		
295	Heat Pump Installation	3 days	Fri 8/7/26	Tue 8/11/26																		
296	Power for Heat Pumps	2 days	Tue 8/11/26	Wed 8/12/26																		
297	HVAC Controls	1 day	Thu 8/13/26	Thu 8/13/26																		
298	Adjust Duct Work	1 day	Wed 8/12/26	Wed 8/12/26																		
299	Install Grid	1 day	Thu 8/13/26	Thu 8/13/26																		
300	Install light fixture	1 day	Fri 8/14/26	Fri 8/14/26																		
301	Install ceiling tile	1 day	Mon 8/17/26	Mon 8/17/26																		
302	Rough in for Special Systems	3 days	Wed 8/5/26	Fri 8/7/26																		
303	Fire Alarm Devices	3 days	Fri 8/14/26	Tue 8/18/26																		
304	PA Devices	3 days	Fri 8/14/26	Tue 8/18/26																		
305	Final Clean Up	1 day	Wed 8/19/26	Wed 8/19/26																		
306	Final Inspections	9 days	Tue 8/18/26	Fri 8/28/26																		
307	Mechanical Final	1 day	Tue 8/18/26	Tue 8/18/26																		
308	Electrical Final	1 day	Wed 8/19/26	Wed 8/19/26																		
309	Fire Alarm Final	1 day	Wed 8/19/26	Wed 8/19/26																		
310	Fire Final	1 day	Thu 8/20/26	Thu 8/20/26																		
311	Building Final	1 day	Fri 8/21/26	Fri 8/21/26																		
312	Certificate of Completion	1 day	Mon 8/24/26	Mon 8/24/26																		
313	Punch List	5 days	Thu 8/20/26	Wed 8/26/26																		
314	CISD Move In	2 days	Thu 8/27/26	Fri 8/28/26																		
315	New Secure Vestibule Phase 1B	34 days	Mon 11/17/25	Thu 1/1/26																		
316	Materials	20 days	Mon 11/17/25	Fri 12/12/25																		
317	Framing	2 days	Mon 12/15/25	Tue 12/16/25																		
318	Door Frame	1 day	Mon 12/15/25	Mon 12/15/25																		
319	Window Frame	1 day	Mon 12/15/25	Mon 12/15/25																		
320	Electrical Rough In	1 day	Wed 12/17/25	Wed 12/17/25																		
321	Rough Carpentry	1 day	Thu 12/18/25	Thu 12/18/25																		
322	Drywall Tape and Bed	3 days	Fri 12/19/25	Tue 12/23/25																		
323	Paint	1 day	Wed 12/24/25	Wed 12/24/25																		
324	Ceiling Grid	1 day	Thu 12/25/25	Thu 12/25/25																		
325	Electrical Trim	1 day	Fri 12/26/25	Fri 12/26/25																		
326	Light Fixture	1 day	Fri 12/26/25	Fri 12/26/25																		
327	Supply and Return	1 day	Fri 12/26/25	Fri 12/26/25																		
328	Fire Alarm	1 day	Mon 12/29/25	Mon 12/29/25																		
329	Ceiling Tile	1 day	Tue 12/30/25	Tue 12/30/25																		
330	Flooring	1 day	Wed 12/31/25	Wed 12/31/25																		
331	Millwork	1 day	Thu 1/1/26	Thu 1/1/26																		
332	Door and Hardware	1 day	Thu 1/1/26	Thu 1/1/26																		
333	Building Letters w/Lead Time	5 days	Mon 12/15/25	Fri 12/19/25																		
334	Glass with Security Film	1 day	Tue 12/16/25	Tue 12/16/25																		
335	New Security Film Existing Storefront	7 days	Wed 12/17/25	Thu 12/25/25																		
336	Exterior	15 days	Wed 11/26/25	Tue 12/16/25																		
337	Demolition	1 day	Wed 11/26/25	Wed 11/26/25																		
338	Earthwork	3 days	Thu 11/27/25	Mon 12/1/25																		
339	Sidewalks	8 days	Tue 12/2/25	Thu 12/11/25																		
Project: Schedule Canutillo HS U Date: Thu 11/13/25 Task Split Milestone ◆ Summary Project Summary Inactive Task Inactive Milestone Inactive Summary Manual Task ◇ Duration-only Manual Summary Rollup Manual Summary Start-only Finish-only External Tasks ┌ ┐ External Milestone Deadline Critical ◇ ↓ Critical Split Progress Manual Progress 																						

ID	Task Name	Duration	Start	Finish	Aug	Sep	Qtr 4, 2025 Oct	Nov	Dec	Qtr 1, 2026 Jan	Feb	Mar	Qtr 2, 2026 Apr	May	Jun	Qtr 3, 2026 Jul	Aug	Sep	Qtr 4, 2026 Oct	Nov	Dec	Qtr 1, 2027 Jan
340	New Signs	1 day	Fri 12/12/25	Fri 12/12/25																		
341	Irrigation/Landscaping	2 days	Mon 12/15/25	Tue 12/16/25																		
342	Punch List	5 days	Fri 12/26/25	Thu 1/1/26																		
343	CTE Room Phase 2B	32 days	Wed 12/17/25	Thu 1/29/26																		
344	CISD Move Out	2 days	Wed 12/17/25	Thu 12/18/25																		
345	Demolition	5 days	Fri 12/19/25	Thu 12/25/25																		
346	Framing New Windows	2 days	Fri 12/26/25	Mon 12/29/25																		
347	Window Frames	1 day	Tue 12/30/25	Tue 12/30/25																		
348	Plumbing Rough In	5 days	Fri 12/26/25	Thu 1/1/26																		
349	Concrete Slab	3 days	Fri 1/2/26	Tue 1/6/26																		
350	Electrical Rough In	3 days	Tue 12/30/25	Thu 1/1/26																		
351	Plumbing Top Out	3 days	Tue 12/30/25	Thu 1/1/26																		
352	Drywall Tape and Bed	4 days	Fri 1/2/26	Wed 1/7/26																		
353	Paint	2 days	Thu 1/8/26	Fri 1/9/26																		
354	Flooring	5 days	Mon 1/12/26	Fri 1/16/26																		
355	Millwork	3 days	Mon 1/19/26	Wed 1/21/26																		
356	Plumbing Final	2 days	Mon 1/19/26	Tue 1/20/26																		
357	Final Clean Up	2 days	Wed 1/21/26	Thu 1/22/26																		
358	Final Inspections	5 days	Fri 1/23/26	Thu 1/29/26																		
359	Fire Final	1 day	Fri 1/23/26	Fri 1/23/26																		
360	Building Final	1 day	Mon 1/26/26	Mon 1/26/26																		
361	Certificate of Completion	1 day	Tue 1/27/26	Tue 1/27/26																		
362	CISD Move In	2 days	Wed 1/28/26	Thu 1/29/26																		
363	Punch List	5 days	Fri 1/23/26	Thu 1/29/26																		
364	New Gasket Replacement	30 days	Fri 12/26/25	Thu 2/5/26																		
365	Demolition	5 days	Fri 12/26/25	Thu 1/1/26																		
366	New Gaskets	15 days	Fri 1/2/26	Thu 1/22/26																		
367	Joint Sealant	5 days	Fri 1/23/26	Thu 1/29/26																		
368	Punch List	5 days	Fri 1/30/26	Thu 2/5/26																		
369	TXDOT Sidewalk	40 days	Fri 1/2/26	Thu 2/26/26																		
370	Traffic Control	40 days	Fri 1/2/26	Thu 2/26/26																		
371	Earthwork	10 days	Fri 1/2/26	Thu 1/15/26																		
372	Sidewalk Form	10 days	Fri 1/16/26	Thu 1/29/26																		
373	Inspection	1 day	Fri 1/30/26	Fri 1/30/26																		
374	Sidewalk	7 days	Mon 2/2/26	Tue 2/10/26																		
375	Joint Sealant	3 days	Wed 2/11/26	Fri 2/13/26																		
376	Punch List	5 days	Mon 2/16/26	Fri 2/20/26																		
377	Plaza Lighting & Stripping Phase 3B	28 days	Wed 2/11/26	Fri 3/20/26																		
378	Demolitions of Light Poles	3 days	Wed 2/11/26	Fri 2/13/26																		
379	Electrical Underground	3 days	Mon 2/16/26	Wed 2/18/26																		
380	Light Pole Bases	5 days	Thu 2/26/26	Wed 3/4/26																		
381	Electrical Rough In	5 days	Thu 2/19/26	Wed 2/25/26																		
382	New Light Poles	6 days	Thu 3/5/26	Thu 3/12/26																		
383	Patch and Repair Around Light Poles	3 days	Thu 3/5/26	Mon 3/9/26																		
384	Stripping	2 days	Tue 3/10/26	Wed 3/11/26																		
385	Irrigation/Landscaping	2 days	Thu 3/12/26	Fri 3/13/26																		
386	Punch List	5 days	Mon 3/16/26	Fri 3/20/26																		
387	Roof	170 days	Mon 11/17/25	Fri 7/10/26																		
388	Materials	40 days	Mon 11/17/25	Fri 1/9/26																		
389	Roof Drains	15 days	Mon 1/12/26	Fri 1/30/26																		
390	Metal Coping Demolition	20 days	Mon 1/12/26	Fri 2/6/26																		
391	Rough Carpentry	20 days	Mon 2/9/26	Fri 3/6/26																		
392	Roof	60 days	Mon 3/9/26	Fri 5/29/26																		
393	Metal Coping	20 days	Mon 6/1/26	Fri 6/26/26																		
394	Punch List	10 days	Mon 6/29/26	Fri 7/10/26																		

Project: Schedule Canutillo HS U

Date: Thu 11/13/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

Page 7
