C	Activity ID	Activity Name	Start	Finish
		GES School Renovation DD 2025-10-21 UP02	22-Oct-24 A	28-Sep-26
		PRECONSTRUCTION PHASE	22-Oct-24 A	28-Sep-26
		Milestones	22-Oct-24 A	28-Sep-26
	GESM1000	Design NTP	22-Oct-24 A	
	GESM1030	Schematic Design Complete		03-Feb-25 A
	GESM1040	Finish Design		19-May-25 A
	GESM1340	Bid Advertisement Sunday 1	13-Jun-25 A	13-Jun-25 A
	GESM1350	Bid Advertisement Sunday 2	20-Jun-25 A	20-Jun-25 A
	GESM1060	Construction NTP	17-Jul-25 A	
	GESM1330	Submit GMP to Canutillo ISD		30-Sep-25
	GESM1190	Substantial Completion		17-Sep-26
	GESM1220	Final Completion		28-Sep-26
		Design Development	22-Oct-24 A	19-May-25 A
	GESD1010	Schematic Design Development	22-Oct-24 A	03-Feb-25 A
	GESD1040	50% Construction Design	04-Feb-25 A	26-Mar-25 A
	GESD1030	100% Construction Design	27-Mar-25 A	19-May-25 A
		JFC Preconstruction	19-May-25 A	11-Dec-25
	GESP1110	Kick Off Meeting	19-May-25 A	19-May-25 A
	GESP1070	Construction Permit	20-May-25 A	17-Jun-25 A
	GESP1300	JFC Design Review	21-May-25 A	11-Jun-25 A
	GESP1230	JFC Advertise for Bids	12-Jun-25 A	19-Jun-25 A
	GESP1310	Pre-Bid Meeting	16-Jun-25 A	16-Jun-25 A
	GESP1250	Bid -Process Questions	17-Jun-25 A	24-Jun-25 A
	GESP1260	JFC Receives Bids	25-Jun-25 A	30-Jun-25 A
	GESP1270	JFC Prepares GMP	01-Jul-25 A	15-Jul-25 A
	GESP1280	Canutillo ISD - Board Review and Approval	16-Jul-25 A	16-Jul-25 A
	GESP1290	Canutillo ISD Issues NTP	16-Jul-25 A	16-Jul-25 A
	GESP1100	Contract Amended	17-Jul-25 A	23-Jul-25 A
		Submittals	17-Jul-25 A	11-Nov-25
	GESS1080	Submittal Register Log	17-Jul-25 A	03-Sep-25 A
	GESSA1090	Process Submittals	03-Sep-25 A	11-Nov-25
		Procurement	23-Sep-25 A	11-Dec-25
	GESS1120	Material Procurment	23-Sep-25 A	11-Dec-25
	GESS1300	Procure HVAC Equipment	30-Sep-25 A	24-Nov-25
		CONSTRUCTION PHASE	24-Jul-25 A	27-Aug-26
	GESM1180	Subcontract Development	24-Jul-25 A	20-Aug-25 A
	GESM1200	Area Turnover	21-Aug-25 A	26-Aug-25 A
	GESM1210	Initial Condition Report	27-Aug-25 A	29-Aug-25 A
	GESM1130	Mobilization	02-Sep-25 A	08-Sep-25 A
	GESM1140	HVAC Controls	14-Aug-26	20-Aug-26
	GESM1170	Replace Designated Coping and Flashing	21-Aug-26	27-Aug-26
	GESM1150	Designated Roof Repairs	21-Aug-26	27-Aug-26
	GESM1160	Remove Existing and Install New Walking Pads	21-Aug-26	27-Aug-26
		Canutillo ISD Activities	15-Dec-25	14-Jul-26
	GESI1000	Transition Area 400 to Area 300 PH 1	15-Dec-25	19-Dec-25

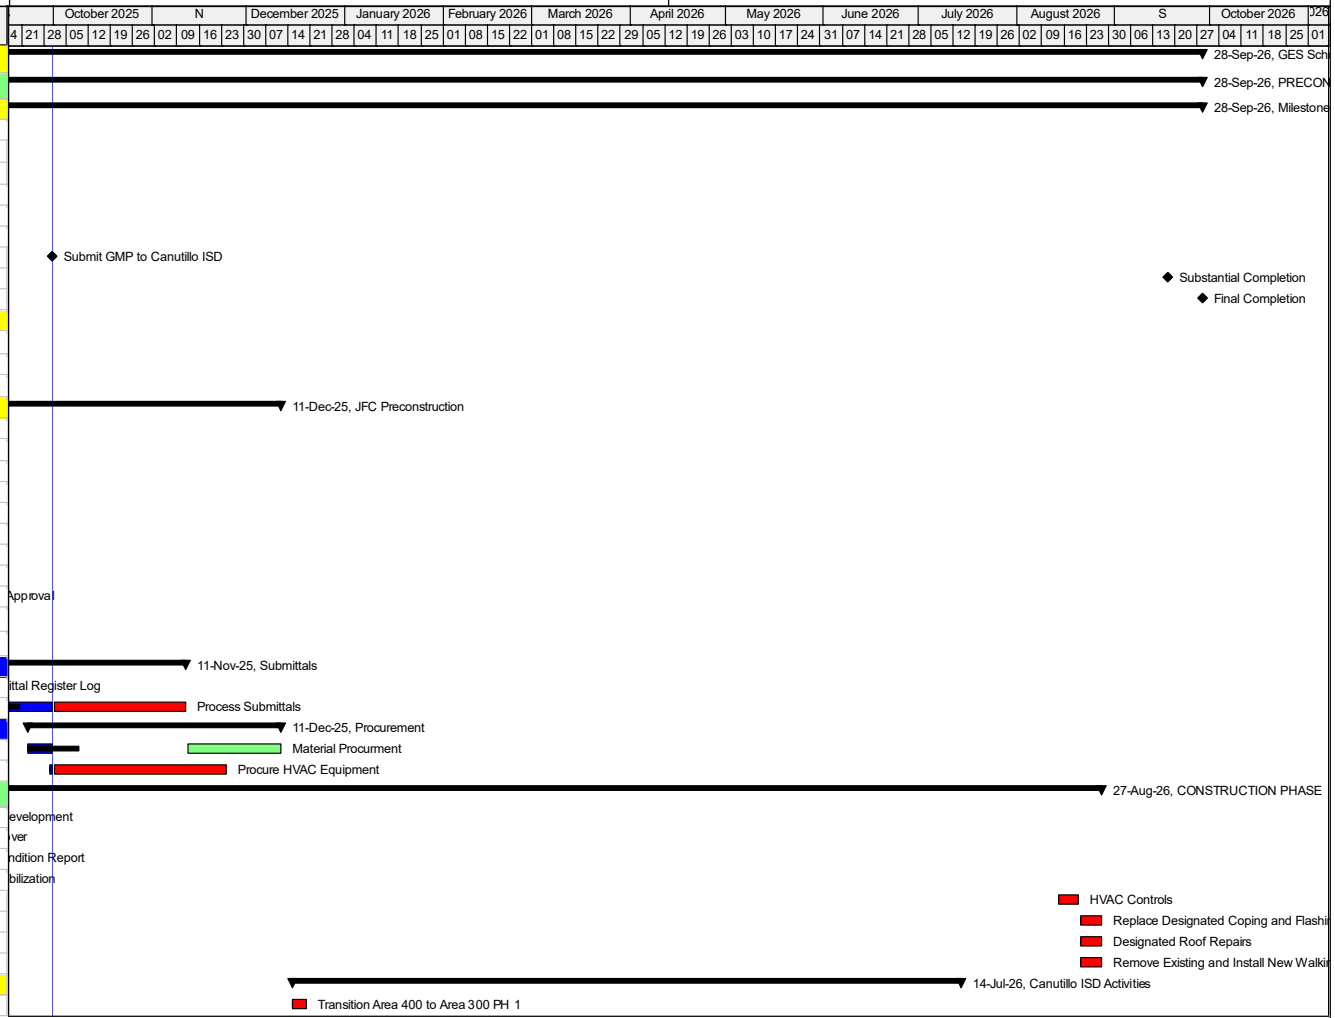

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Start Constraint
Finish Constraint
Milestone
% Complete
Summary

Canutillo ISD - Gonzalo and Sofia Garcia ES Renovation
GMP Schedule

JORDAN FOSTER CONSTRUCTION

C	Activity ID	Activity Name	Start	Finish
	GESI1010	Transition Area 300 PH 1 to 300 PH 2	27-Jan-26	02-Feb-26
	GESI1020	Transition Area 300 PH 2 to Area 200 PH 1	09-Mar-26	13-Mar-26
	GESI1030	Transition Area 200 PH1 to Area 200 PH2	17-Apr-26	23-Apr-26
	GESI1050	Transition Area 200 PH 2 to Area 100	26-May-26	01-Jun-26
	GESI1040	Transition Area Area 100 to Area 500/600	08-Jul-26	14-Jul-26
	Secure Vestibule		18-Dec-25	13-Jan-26
	GES1150	Mobilization/Existing Condition Report	18-Dec-25*	19-Dec-25
	GES1000	Partial Demo Ceiling Tile, Wall and Flooring	19-Dec-25	19-Dec-25
	GES1010	Modify Existing Storefront	22-Dec-25	23-Dec-25
	GES1020	MEP Rough-in for New Storefront and Doors	22-Dec-25	23-Dec-25
	GES1100	Install Canopies (Alt 7)	22-Dec-25	07-Jan-26
	GES1110	New Pedestrian Gate (Alt 5)	22-Dec-25	07-Jan-26
	GES1030	Fur-down Construction	24-Dec-25	29-Dec-25
	GES1040	Storefront Installation	30-Dec-25	31-Dec-25
	GES1050	Door and Door Harware Installation	02-Jan-26	02-Jan-26
	GES1060	Patch and Paint Walls	05-Jan-26	06-Jan-26
	GES1070	Paint Storefront	07-Jan-26	08-Jan-26
	GES1080	Install Ceiling Grid and Tiles	09-Jan-26	09-Jan-26
	GES1090	Install Flooring	12-Jan-26	12-Jan-26
	GES1160	Demobilization	13-Jan-26	13-Jan-26
	Area 400		01-Oct-25	12-Dec-25
	GES1200	Area 400 Mobilization/Existing Condition Report	01-Oct-25	01-Oct-25
	GES1210	Area 400 MEP Demolition	02-Oct-25	06-Oct-25
	GES1280	Area 400 Remove and Dispose of Existing RTUs	02-Oct-25	13-Oct-25
	GES1190	Area 400 Remove Selected Ceiling Grid and Tiles	02-Oct-25	03-Oct-25
	GES1230	Area 400 Designated Fire Alarm Demolition	07-Oct-25	09-Oct-25
	GES1240	Area 400 MEP Rough in	07-Oct-25	09-Oct-25
	GES1220	Area 400 Special Systems Demolition	07-Oct-25	08-Oct-25
	GES1250	Area 400 Special Systems Rough in	07-Oct-25	09-Oct-25
	GES1260	Area 400 Data and Electrical Cable/Wire Pull	09-Oct-25	14-Oct-25
	GES1290	Area 400 Install Special Systems	10-Oct-25	14-Oct-25
	GES1270	Area 400 Fire Alarm Rough-in	10-Oct-25	13-Oct-25
	GES1310	Area 400 Install New Fire Alarm System	14-Oct-25	16-Oct-25
	GES1320	Area 400 Replace Damaged Ceiling Tiles	17-Oct-25	17-Oct-25
	GES1300	Area 400 Install Roof Curb Adapaters	25-Nov-25	01-Dec-25
	GES1340	Area 400 Install New RTUs	02-Dec-25	11-Dec-25
	GES1330	Area 400 Install Temporary HVAC Controls	03-Dec-25	04-Dec-25
	GES1350	Area 400 Demobilization	12-Dec-25	12-Dec-25
	Area 300 Phase 1		22-Dec-25	26-Jan-26
	GESA3360	Area 300-1 Mobilization/Exsiting Conditions Report	22-Dec-25	22-Dec-25
	GESA3440	Area 300-1 Remove and Dispose of Existing RTUs	23-Dec-25	06-Jan-26
	GESA3370	Area 300-1 Remove Selected Ceiling Grid and Tiles	23-Dec-25	23-Dec-25
	GESA3380	Area 300-1 MEP Demolition	24-Dec-25	30-Dec-25
	GESA3430	Area 300-1 Install Special Systems	31-Dec-25	06-Jan-26
	GESA3390	Area 300-1 Special Systems Rough-in	31-Dec-25	05-Jan-26
	GESA3400	Area 300-1 Water Heater Installation as Required (Alt 2)	31-Dec-25	05-Jan-26

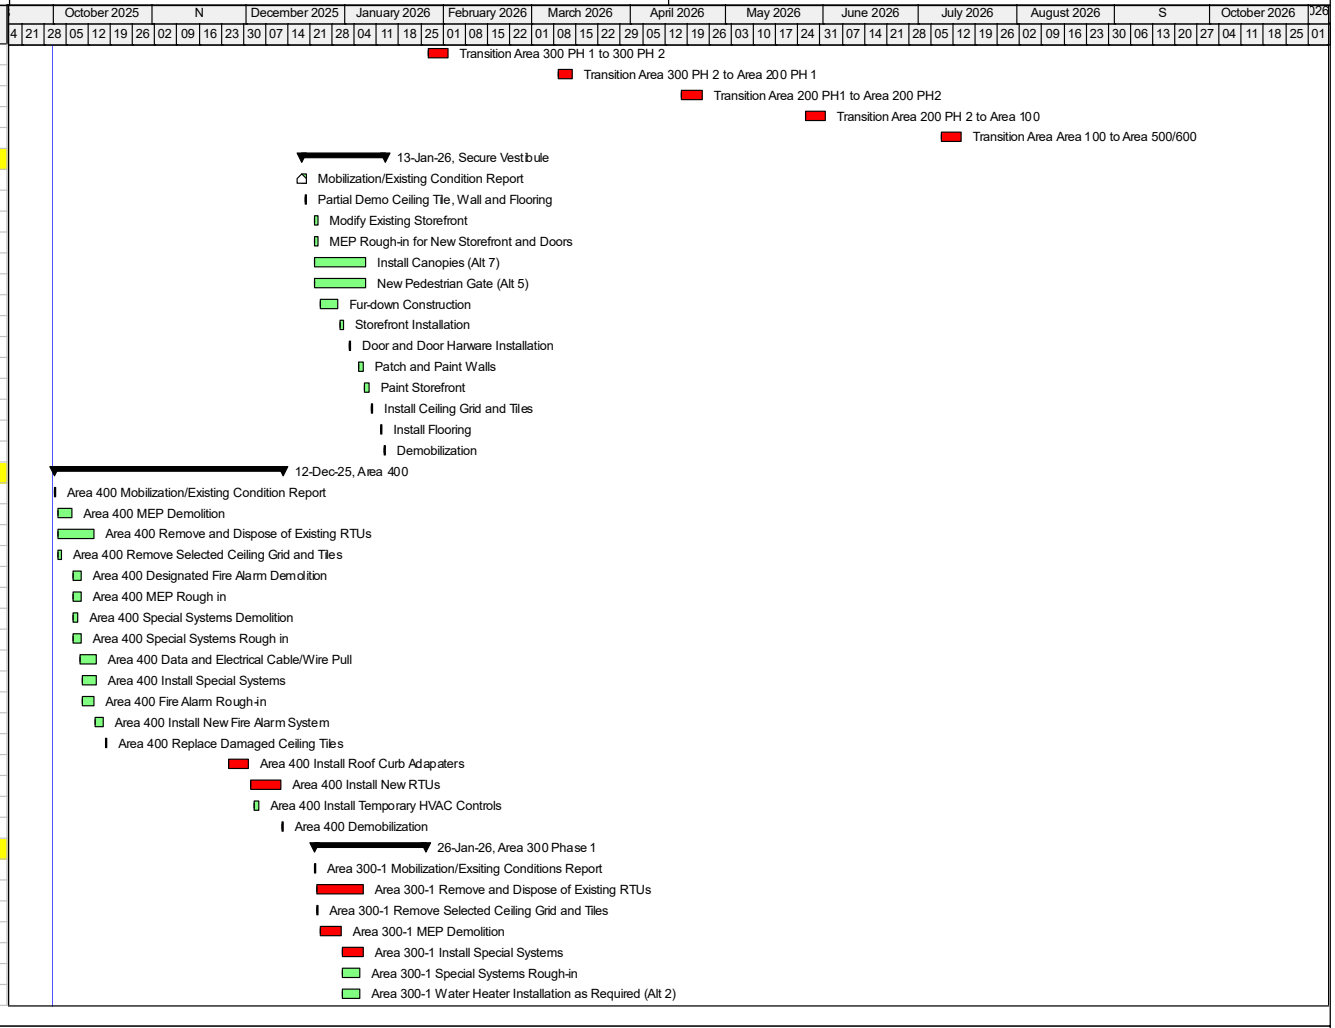

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Start Constraint
Finish Constraint
Milestone
% Complete
Summary

Canutillo ISD - Gonzalo and Sofia Garcia ES Renovation
GMP Schedule

JORDAN FOSTER CONSTRUCTION

C	Activity ID	Activity Name	Start	Finish
	GESA3410	Area 300-1 Designated Fire Alarm Demolition	31-Dec-25	05-Jan-26
	GESA3420	Area 300-1 Special Systems Demolition	31-Dec-25	05-Jan-26
	GESA3450	Area 300-1 Data and Electrical Cable/Wire Pull	06-Jan-26	08-Jan-26
	GESA3460	Area 300-1 Fire Alarm Rough-in	06-Jan-26	08-Jan-26
	GESA3470	Area 300-1 Install Roof Curb Adapaters	07-Jan-26	09-Jan-26
	GESA3480	Area 300-1 Install New Fire Alarm System	09-Jan-26	13-Jan-26
	GESA3500	Area 300-1 Install New RTUs	12-Jan-26	21-Jan-26
	GESA3490	Area 300-1 Replace Damaged Ceiling Tiles	14-Jan-26	14-Jan-26
	GESA3510	Area 300-1 Install Temporary HVAC Controls	22-Jan-26	23-Jan-26
	GESA3520	Area 300-1 Demobilization	26-Jan-26	26-Jan-26
	Area 300 Phase 2		03-Feb-26	06-Mar-26
	GESB3000	Area 300-2 Mobilization/Exsiting Conditions Report	03-Feb-26	03-Feb-26
	GESB3080	Area 300-2 Remove and Dispose of Existing RTUs	04-Feb-26	10-Feb-26
	GESB3010	Area 300-2 Remove Selected Ceiling Grid and Tiles	04-Feb-26	05-Feb-26
	GESB3020	Area 300-2 MEP Demolition	06-Feb-26	10-Feb-26
	GESB3070	Area 300-2 Install Special Systems	11-Feb-26	16-Feb-26
	GESB3030	Area 300-2 Special Systems Rough-in	11-Feb-26	13-Feb-26
	GESB3040	Area 300-2 Water Heater Installation as Required (Alt 2)	11-Feb-26	13-Feb-26
	GESB3050	Area 300-2 Designated Fire Alarm Demolition	11-Feb-26	13-Feb-26
	GESB3060	Area 300-2 Special Systems Demolition	11-Feb-26	13-Feb-26
	GESB3090	Area 300-2 Data and Electrical Cable/Wire Pull	16-Feb-26	18-Feb-26
	GESB3100	Area 300-2 Fire Alarm Rough-in	16-Feb-26	18-Feb-26
	GESB3110	Area 300-2 Install Roof Curb Adapaters	17-Feb-26	19-Feb-26
	GESB3120	Area 300-2 Install New Fire Alarm System	19-Feb-26	23-Feb-26
	GESB3140	Area 300-2 Install New RTUs	20-Feb-26	03-Mar-26
	GESB3130	Area 300-2 Replace Damaged Ceiling Tiles	24-Feb-26	24-Feb-26
	GESB3150	Area 300-2 Install Temporary HVAC Controls	04-Mar-26	05-Mar-26
	GESB3160	Area 300-2 Demobilization	06-Mar-26	06-Mar-26
	Area 300 Bathroom (Alt #3)		22-Dec-25	27-Feb-26
	A1000	Site Work, Excavation and Earthwork	22-Dec-25	24-Dec-25
	A1020	Slab on Grade	29-Dec-25	02-Jan-26
	A1030	Concrete Curing and Sealing	05-Jan-26	07-Jan-26
	A1040	Wall Framing	08-Jan-26	12-Jan-26
	A1050	Plumbing and Electrical in Wall Rough-in	13-Jan-26	15-Jan-26
	A1060	Roof Framing	16-Jan-26	21-Jan-26
	A1070	Install Roofing System (Dry-in)	22-Jan-26	26-Jan-26
	A1080	EEFIS Sytem	27-Jan-26	30-Jan-26
	A1090	Install Cement Board	02-Feb-26	03-Feb-26
	A1100	Hard Ceiling Installation	04-Feb-26	09-Feb-26
	A1110	Interior and Exterior Painting	10-Feb-26	12-Feb-26
	A1120	Wall Tile Installation	13-Feb-26	17-Feb-26
	A1130	Fixture Installation	18-Feb-26	20-Feb-26
	A1140	Removal and Installation of Exterior Doors	23-Feb-26	24-Feb-26
	A1010	Underground MEP Rough-in	25-Feb-26	27-Feb-26
	Area 200 Phase 1		16-Mar-26	16-Apr-26
	GESA2190	Area 200-1 Mobilization/Exsiting Conditions Report	16-Mar-26	16-Mar-26

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Start Constraint
Finish Constraint
Milestone
% Complete
Summary

C	Activity ID	Activity Name	Start	Finish
	GESA2270	Area 200-1 Remove and Dispose of Existing RTUs	17-Mar-26	23-Mar-26
	GESA2200	Area 200-1 Remove Selected Ceiling Grid and Tiles	17-Mar-26	17-Mar-26
	GESA2210	Area 200-1 MEP Demolition	18-Mar-26	20-Mar-26
	GESA2260	Area 200-1 Install Special Systems	23-Mar-26	26-Mar-26
	GESA2220	Area 200-1 Special Systems Rough-in	23-Mar-26	25-Mar-26
	GESA2230	Area 200-1 Water Heater Installation as Required (Alt 2)	23-Mar-26	25-Mar-26
	GESA2240	Area 200-1 Designated Fire Alarm Demolition	23-Mar-26	25-Mar-26
	GESA2250	Area 200-1 Special Systems Demolition	23-Mar-26	25-Mar-26
	GESA2280	Area 200-1 Data and Electrical Cable/Wire Pull	26-Mar-26	30-Mar-26
	GESA2290	Area 200-1 Fire Alarm Rough-in	26-Mar-26	30-Mar-26
	GESA2300	Area 200-1 Install Roof Curb Adapaters	27-Mar-26	31-Mar-26
	GESA2310	Area 200-1 Install New Fire Alarm System	31-Mar-26	02-Apr-26
	GESA2330	Area 200-1 Install New RTUs	01-Apr-26	13-Apr-26
	GESA2320	Area 200-1 Replace Damaged Ceiling Tiles	06-Apr-26	06-Apr-26
	GESA2340	Area 200-1 Install Temporary HVAC Controls	14-Apr-26	15-Apr-26
	GESA2350	Area 200-1 Demobilization	16-Apr-26	16-Apr-26
	Area 200 Phase 2		24-Apr-26	22-May-26
	GESB2180	Area 200-2 Mobilization/Existing Condition Report	24-Apr-26	24-Apr-26
	GESB2190	Area 200-2 MEP Demolition	27-Apr-26	01-May-26
	GESB2260	Area 200-2 Remove and Dispose of Existing RTUs	27-Apr-26	06-May-26
	GESB2170	Area 200-2 Remove Selected Ceiling Grid and Tiles	27-Apr-26	01-May-26
	GESB2210	Area 200-2 Designated Fire Alarm Demolition	04-May-26	06-May-26
	GESB2220	Area 200-2 Water Heater Installation as Required (Alt 2)	04-May-26	06-May-26
	GESB2200	Area 200-2 Special Systems Demolition	04-May-26	05-May-26
	GESB2230	Area 200-2 Special Systems Rough in	04-May-26	06-May-26
	GESB2240	Area 200-2 Data and Electrical Cable/Wire Pull	06-May-26	11-May-26
	GESB2280	Area 200-2Install Roof Curb Adapaters	07-May-26	11-May-26
	GESB2270	Area 200-2 Install Special Systems	07-May-26	11-May-26
	GESB2250	Area 200-2 Fire Alarm Rough-in	07-May-26	08-May-26
	GESB2290	Area 200-2 Install New Fire Alarm System	11-May-26	13-May-26
	GESB2320	Area 200-2 Install New RTUs	12-May-26	21-May-26
	GESB2310	Area 200-2 Install Temporary HVAC Controls	13-May-26	14-May-26
	GESB2300	Area 200-2 Replace Damaged Ceiling Tiles	14-May-26	14-May-26
	GESB2330	Area 200-2 Demobilization	22-May-26	22-May-26
	Area 200 Bathroom (Alt #2)		29-Dec-25	04-Mar-26
	A1150	Site Work, Excavation and Earthwork	29-Dec-25	31-Dec-25
	A1290	Underground MEP Rough-in	02-Jan-26	06-Jan-26
	A1160	Slab on Grade	07-Jan-26	12-Jan-26
	A1170	Concrete Curing and Sealing	13-Jan-26	15-Jan-26
	A1180	Wall Framing	16-Jan-26	20-Jan-26
	A1190	Plumbing and Electrical in Wall Rough-in	21-Jan-26	23-Jan-26
	A1200	Roof Framing	26-Jan-26	29-Jan-26
	A1210	Install Roofing System (Dry-in)	30-Jan-26	03-Feb-26
	A1220	EEFIS Sytem	04-Feb-26	09-Feb-26
	A1230	Install Cement Board	10-Feb-26	11-Feb-26
	A1240	Hard Ceiling Installation	12-Feb-26	17-Feb-26

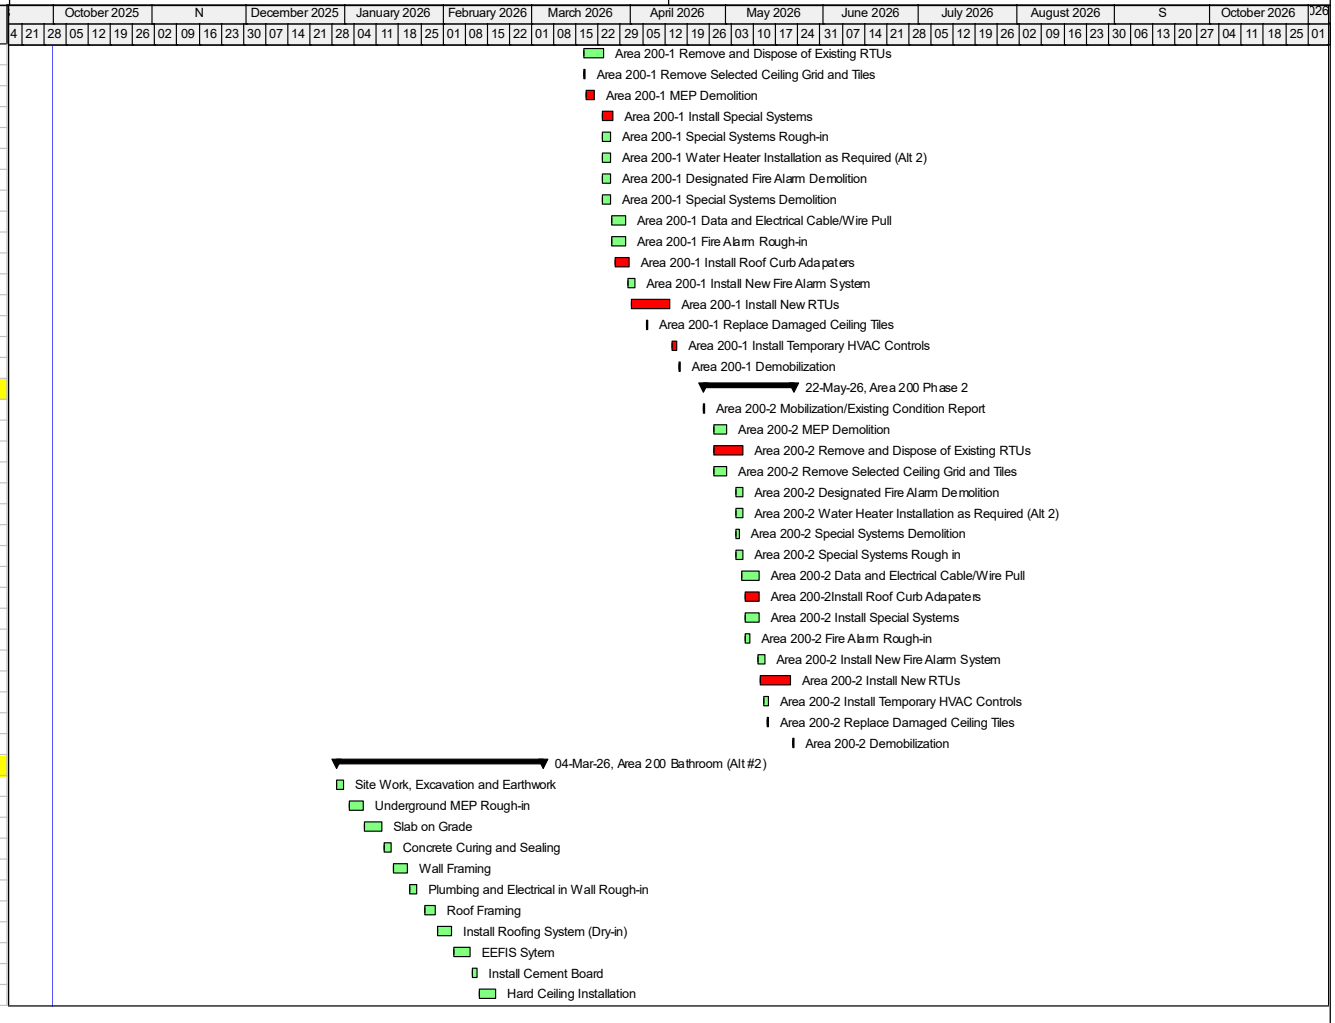

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Start Constraint
Finish Constraint
Milestone
% Complete
Summary

Canutillo ISD - Gonzalo and Sofia Garcia ES Renovation
GMP Schedule

JORDAN FOSTER CONSTRUCTION

C	Activity ID	Activity Name	Start	Finish
	A1250	Interior and Exterior Painting	18-Feb-26	20-Feb-26
	A1260	Wall Tile Installation	23-Feb-26	25-Feb-26
	A1270	Fixture Installation	26-Feb-26	02-Mar-26
	A1280	Removal and Installation of Exterior Doors	03-Mar-26	04-Mar-26
	Area 100		02-Jun-26	07-Jul-26
	GES4200	Area 100 Mobilization/Existing Condition Report	02-Jun-26	02-Jun-26
	GES4210	Area 100 MEP Demolition	03-Jun-26	04-Jun-26
	GES4190	Area 100 Remove Selected Ceiling Grid and Tiles	03-Jun-26	04-Jun-26
	GES4280	Area 100 Remove and Dispose of Existing RTUs	05-Jun-26	16-Jun-26
	GES4230	Area 100 Designated Fire Alarm Demolition	05-Jun-26	09-Jun-26
	GES4240	Area 100 Water Heater Installation as Required (Alt 2)	05-Jun-26	09-Jun-26
	GES4220	Area 100 Special Systems Demolition	05-Jun-26	08-Jun-26
	GES4250	Area 100 Special Systems Rough in	05-Jun-26	09-Jun-26
	GES4260	Area 100 Data and Electrical Cable/Wire Pull	09-Jun-26	12-Jun-26
	GES4290	Area 100 Install Special Systems	10-Jun-26	12-Jun-26
	GES4270	Area 100 Fire Alarm Rough-in	10-Jun-26	11-Jun-26
	GES4310	Area 100 Install New Fire Alarm System	12-Jun-26	15-Jun-26
	GES4320	Area 100 Replace Damaged Ceiling Tiles	16-Jun-26	16-Jun-26
	GES4300	Area 100 Install Roof Curb Adapaters	17-Jun-26	19-Jun-26
	GES4340	Area 100 Install New RTUs	22-Jun-26	06-Jul-26
	GES4330	Area 100 Install Temporary HVAC Controls	25-Jun-26	26-Jun-26
	GES4350	Area 100 Demobilization	07-Jul-26	07-Jul-26
	Area 500/600		15-Jul-26	13-Aug-26
	GES5370	Area 500/600 Mobilization/Existing Condition Report	15-Jul-26	15-Jul-26
	GES5380	Area 500/600 MEP Demolition	16-Jul-26	20-Jul-26
	GES5360	Area 500/600 Remove Selected Ceiling Grid and Tiles	16-Jul-26	17-Jul-26
	GES5450	Area 500/600 Remove and Dispose of Existing RTUs	21-Jul-26	28-Jul-26
	GES5400	Area 500/600 Designated Fire Alarm Demolition	21-Jul-26	23-Jul-26
	GES5410	Area 500/600 Water Heater Installation (Alt 2)	21-Jul-26	23-Jul-26
	GES5390	Area 500/600 Special Systems Demolition	21-Jul-26	22-Jul-26
	GES5420	Area 500/600 Special Systems Rough in	21-Jul-26	23-Jul-26
	GES5430	Area 500/600 Data and Electrical Cable/Wire Pull	23-Jul-26	27-Jul-26
	GES5460	Area 500/600 Install Special Systems	24-Jul-26	29-Jul-26
	GES5440	Area 500/600 Fire Alarm Rough-in	24-Jul-26	27-Jul-26
	GES5480	Area 500/600 Install New Fire Alarm System	28-Jul-26	29-Jul-26
	GES5470	Area 500/600 Install Roof Curb Adapaters	29-Jul-26	31-Jul-26
	GES5490	Area 500/600 Replace Damaged Ceiling Tiles	30-Jul-26	30-Jul-26
	GES5510	Area 500/600 Install New RTUs	03-Aug-26	12-Aug-26
	GES5500	Area 500/600 Install Temporary HVAC Controls	04-Aug-26	05-Aug-26
	GES5520	Area 500/600 Demobilization	13-Aug-26	13-Aug-26
	CLOSE OUT PHASE		28-Aug-26	28-Sep-26
	GESC1220	Final Cleaning	28-Aug-26	31-Aug-26
	GESC1170	Inspection w/AJH	01-Sep-26	08-Sep-26
	GESC1200	Close Out Package	01-Sep-26	15-Sep-26
	GESC1180	O/A/E Punch List	09-Sep-26	17-Sep-26
	GESC1230	Substantial Completion	17-Sep-26	17-Sep-26

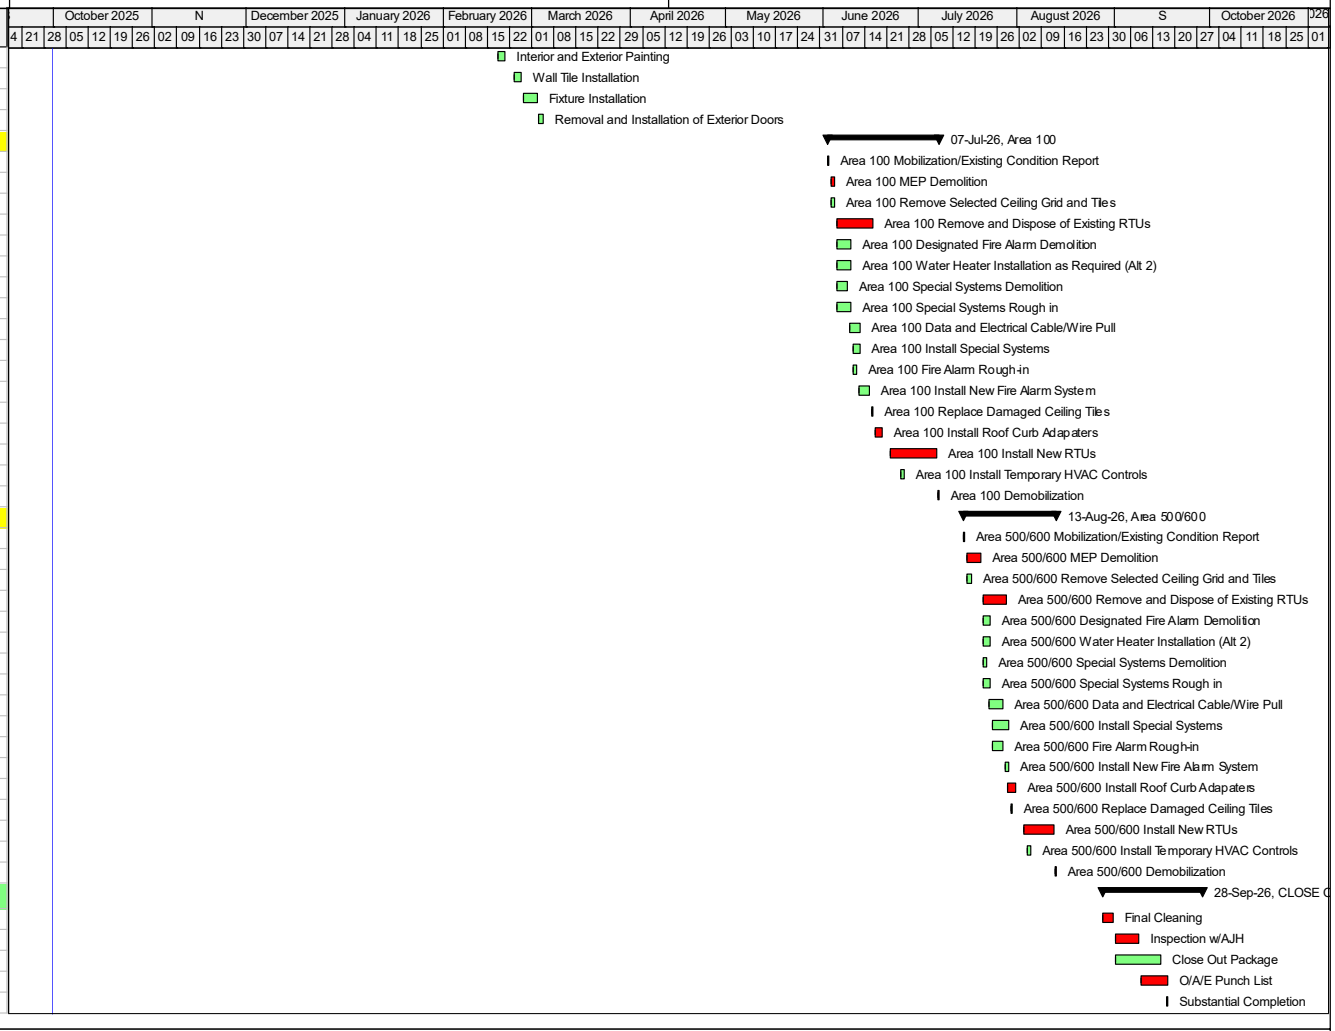

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Start Constraint
Finish Constraint
Milestone
% Complete
Summary

Canutillo ISD - Gonzalo and Sofia Garcia ES Renovation
GMP Schedule

JORDAN FOSTER CONSTRUCTION

C	Activity ID	Activity Name	Start	Finish
	GESC1210	Punch List	18-Sep-26	28-Sep-26
